

Daniel Foister, Jason Gun, Timyathus Spikes, Tyrese Dickson - DTJT Group
Shehenaz Shaik
CSCI 4350
Sprint #10 - 4/16-4/23

Roles:

- Product Owner: Timyathus Spikes
- Scrum Master: Daniel Foister
- Development Team: Jason Gun, Tyrese Dickson

Time Limit: Two Days (4/16, 4/21, 4/23)

Attendance: All group members were present this week.

Project Github Repo: <https://github.com/12061062/StockBuddy>

Sprint Goal:

- The goal for this sprint was to finalize StockBuddy by completing final testing, improving code quality, implementing basic system metrics, and preparing user documentation. These help to make sure the system is stable, well-documented, and ready for final delivery and demonstration.

PBIs/User Stories/To-Do Chosen for Sprint:

- **SCRUM-60:** Perform final system testing to ensure all features function correctly.
 - Estimation: 4 story points
- **SCRUM-61:** Create the user manual describing how to use StockBuddy.
 - Estimation: 4 story points
- **SCRUM-62:** Display simple metrics (total sales, items sold) within the application.
 - Estimation: 4 story points
- **SCRUM-63:** Clean up and refactor code for readability and maintainability.
 - Estimation: 4 story points
- =====
- The PBIs/tasks selected for this sprint were based on our team's average velocity of around 16 story points per sprint from previous sprints. These features were prioritized because they focus on finalizing the system, improving usability, ensuring reliability, and preparing all required deliverables for project completion.

Sprint Planning

- During sprint planning, our team reviewed the backlog and selected/created four PBIs/tasks that aligned well with StockBuddy's current development stage. The tasks were distributed evenly among our team members, and the acceptance criteria were clarified before beginning implementation.

Total Sprint Duration:

- 4 members x 7 hours/week x 1 Week/Sprint = **28 man-hours available**

Tasks Performed:

- Task Name: Perform final system testing to ensure all features function correctly.
- Task Owner: Tyrese Dickson
- Planned Duration: 6 hours
- Actual Duration: 7 hours
- Status: Completed
- Challenges: None

- Lessons Learned: Thorough testing is extremely important for a good product.

-
- Task Name: Create the user manual describing how to use StockBuddy.
 - Task Owner: Timyathus Spikes
 - Planned Duration: 5 hours
 - Actual Duration: 6 hours
 - Status: Completed
 - Challenges: None
 - Lessons Learned: Clear documentation improves usability and user experience.

-
- Task Name: Display simple metrics (total sales, items sold) within the application.
 - Task Owner: Jason Gun
 - Planned Duration: 5 hours
 - Actual Duration: 6 hours
 - Status: Completed
 - Challenges: None
 - Lessons Learned: None

-
- Task Name: Clean up and refactor code for readability and maintainability.
 - Task Owner: Daniel Foister
 - Planned Duration: 5 hours
 - Actual Duration: 6 hours
 - Status: Completed
 - Challenges: None
 - Lessons Learned: Clean and well-structured code improves long-term maintainability.
-

Sprint Review:

- Was the Sprint Goal Achieved?:
 - The Sprint Goal was Achieved.
 - Definition of Done (DoD)
 - Our DoD: All work/code maps to the requirements specified in the Jira Board (backlog) and meets the defined acceptance criteria. Each completed item has been fully implemented, tested, and verified to function correctly within the system. Code has been reviewed by team members, integrated into the main project without conflicts, and does not introduce new defects. Any necessary documentation has been updated, and the feature is considered complete, stable, and ready for demonstration or release.
 - Our team successfully implemented and completed final system testing, created user documentation, implemented basic system metrics, and refactored the codebase for improved readability and maintainability. These improvements ensure the system is fully functional, user-friendly, and ready for final demonstration and submission.
- Focus for the Next Sprint:

- This was the last sprint for our project.
- However, the team will:
 - Prepare for the class demonstration of StockBuddy.
 - Ensure the GitHub repository is fully updated with all documents/deliverables.
- PO/Stakeholder Review:
 - The Product Owner reviewed all completed tasks/backlog items:
 - All system features have been tested and are functioning correctly.
 - A complete user manual has been created for system usage.
 - Basic system metrics are displayed correctly within the application.
 - The codebase has been cleaned up and improved for maintainability.
 - Feedback Provided:
 - Looks good overall.
 - Priority Revisions:
 1. We will no longer be working on this project.
- Testing
 - During this sprint, we conducted final system testing to ensure all features function correctly and that recent changes did not introduce any issues. These tests helped confirm the system is stable and ready for demonstration.
 - Unit Tests:
 - Test that all core system features function correctly after final integration.
 - Test that system metrics display accurate values.
 - Test that the refactored code does not break existing functionality.
 - Test that user workflows operate correctly.

Sprint Retrospective:

- Changes in the Scrum Process:
 - Again, our team does not believe we need to make any changes to the Scrum Process yet, in the context of this Sprint.
- Start: Finalizing documentation and ensuring all deliverables are complete for submission.
- Stop: Making unnecessary changes after features have been finalized.
- Continue: Frequent push requests/commits, clear communication, and consistent task tracking.
- Other Planned Adjustments/Concerns:
 - No major concerns were identified during this sprint.
- Team Velocity:
 - Sprint 1: 12 story points
 - Sprint 2: 16 story points
 - Sprint 3: 18 story points
 - Sprint 4: 17 story points
 - Sprint 5: 17 story points
 - Sprint 6: 16 story points
 - Sprint 7: 16 story points

- Sprint 8: 16 story points
- Sprint 9: 17 story points
- Sprint 10: 16 story points
- =====
- Average Velocity: ~16 story points per sprint

Backlog Grooming

- PBIs/Tasks Added/Removed/Reprioritized
 - We will no longer be working on this project, so nothing was added.
- Definition of Ready (DoR)
 - Our DoR: A backlog item is considered ready when it has clearly defined acceptance criteria, estimated story points, and any dependencies have been identified. The task is well-understood by the team, correctly scoped, and small enough to be completed within a single sprint. All required resources, tools, and information are available, allowing the team to begin work without blockers.

Daily Standup #1:

- Duration: 5 Minutes
- Facilitator: Daniel Foister

=====

Tyrese Dickson

1. **What did I do yesterday?**
I wrapped up working on implementing the triggering of specific functions based on user actions (checkout | update inventory | log transaction).
2. **What do I plan to do today?**
Today, I planned out how to perform final system testing to ensure all features function correctly.
3. **What are any challenges or impediments that I have experienced?**
None

Timyathus Spikes

1. **What did I do yesterday?**
I wrapped up working on refactoring a small feature into a standalone function to simulate a serverless (FaaS) approach.
2. **What do I plan to do today?**
Today, I planned out how to create the user manual describing how to use StockBuddy.
3. **What are any challenges or impediments that I have experienced?**
None

Jason Gun

1. **What did I do yesterday?**
I wrapped up working on identifying parts of the system that could be converted into event-driven functions.
2. **What do I plan to do today?**
Today, I planned out how to display simple metrics (total sales, items sold) within the application.
3. **What are any challenges or impediments that I have experienced?**
None

Daniel Foister

1. **What did I do yesterday?**

I wrapped up working on documenting how the system could transition to a serverless architecture.

2. **What do I plan to do today?**

Today, I planned out how to clean up and refactor code for readability and maintainability.

3. **What are any challenges or impediments that I have experienced?**

None

Daily Standup #2:

- Duration: 5 Minutes
- Facilitator: Daniel Foister

=====

Tyrese Dickson

4. **What did I do yesterday?**

Yesterday, I planned out how to perform final system testing to ensure all features function correctly.

5. **What do I plan to do today?**

Today, I am going to perform final system testing to ensure all features function correctly, which I planned out during the last session.

6. **What are any challenges or impediments that I have experienced?**

None

Timyathus Spikes

4. **What did I do yesterday?**

Yesterday, I planned out how to create the user manual describing how to use StockBuddy.

5. **What do I plan to do today?**

Today, I am going to create the user manual describing how to use StockBuddy, which I planned out during the last session.

6. **What are any challenges or impediments that I have experienced?**

None

Jason Gun

4. **What did I do yesterday?**

Yesterday, I planned out how to display simple metrics (total sales, items sold) within the application.

5. **What do I plan to do today?**

Today, I am going to display simple metrics (total sales, items sold) within the application, which I planned out during the last session.

6. **What are any challenges or impediments that I have experienced?**

None

Daniel Foister

4. **What did I do yesterday?**

Yesterday, I planned out how to clean up and refactor code for readability and maintainability.

5. **What do I plan to do today?**

Today, I am going to begin cleaning up and refactoring code for readability and maintainability.

6. **What are any challenges or impediments that I have experienced?**

None

Daily Standup #3:

- Duration: 5 Minutes
- Facilitator: Daniel Foister

=====

Tyrese Dickson

7. **What did I do yesterday?**

I continued working on performing final system testing to ensure all features function correctly.

8. **What do I plan to do today?**

Complete my assigned task by finishing my project deliverables.

9. **What are any challenges or impediments that I have experienced?**

None

Timyathus Spikes

7. **What did I do yesterday?**

I continued working on creating the user manual describing how to use StockBuddy.

8. **What do I plan to do today?**

Complete my assigned task by finishing my project deliverables.

9. **What are any challenges or impediments that I have experienced?**

None

Jason Gun

7. **What did I do yesterday?**

I continued working on displaying simple metrics (total sales, items sold) within the application.

8. **What do I plan to do today?**

Complete my assigned task by finishing my project deliverables.

9. **What are any challenges or impediments that I have experienced?**

None

Daniel Foister

7. **What did I do yesterday?**

I continued working on cleaning up and refactoring code for readability and maintainability.


8. **What do I plan to do today?**

Complete my assigned task by finishing my project deliverables.

9. **What are any challenges or impediments that I have experienced?**

None

Exported Copy of Scrum Board:

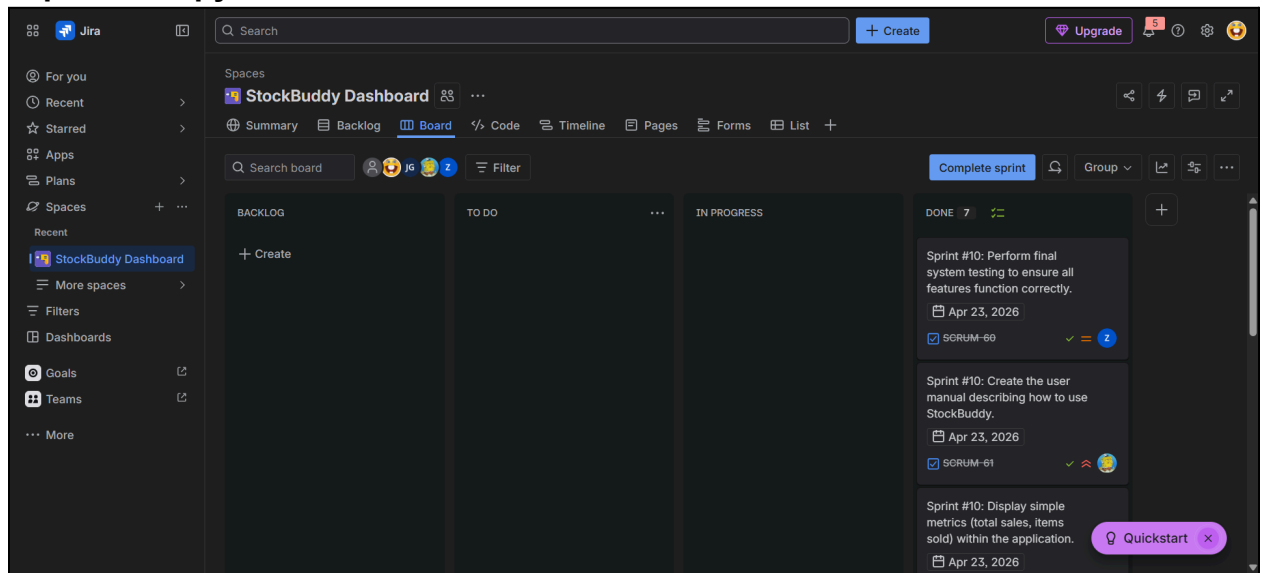

END.
