

Daniel Foister, Jason Gun, Timyathus Spikes, Tyrese Dickson - DTJT Group
Shehenaz Shaik
CSCI 4350
Sprint #2 - 2/12-2/19

Roles:

- Product Owner: Daniel Foister
- Scrum Master: Timyathus Spikes
- Development Team: Jason Gun, Tyrese Dickson

Time Limit: Two Days (2/12, 2/17, 2/19)

Sprint Goal:

- To improve the POS functionality by implementing checkout calculations, cart editing, receipt generation, and role-based authentication. This sprint focused on strengthening the main checkout workflows while improving the overall security via access control.

User Stories/To-Do Chosen for Sprint:

- **SCRUM-23:** Calculate tax & totals upon checkout.
- **SCRUM-24:** Ability to edit the cart by removing items for correction purposes.
- **SCRUM-25:** Send the customer a receipt upon checkout.
- **SCRUM-26:** Incorporate role-based authentication for inventory management and checkout.

Total Sprint Duration:

- 4 members x 9 hours/week x 1 Week/Sprint = **36 man-hours available**

Tasks Performed:

- Task Name: Calculate tax & totals upon checkout.
- Task Owner: Tyrese Dickson
- Planned Duration: 5 hours
- Actual Duration: 7 hours
- Status: Completed
- Challenges: It took me longer than I would have liked to test/refine the tax so that it would be updated automatically when items were removed/added.

=====

- Task Name: Ability to edit the cart by removing items for correction purposes.
- Task Owner: Timyathus Spikes
- Planned Duration: 6 hours
- Actual Duration: 8 hours
- Status: Completed
- Challenges: None

=====

- Task Name: Send the customer a receipt upon checkout.
- Task Owner: Jason Gun
- Planned Duration: 4 hours
- Actual Duration: 5 hours
- Status: Completed
- Challenges: None

=====

- Task Name: Incorporate role-based authentication for inventory management and checkout.
- Task Owner: Daniel Foister
- Planned Duration: 5 hours
- Actual Duration: 6 hours
- Status: Completed
- Challenges: It took me a little while to verify the 'restricted access' for non-admin roles.

=====

Sprint Review:

- Was the Sprint Goal Achieved?:
 - The Sprint Goal was Achieved.
 - Our DoD: Our work/code maps to all requirements specified in the Jira Board (backlog).
 - We successfully implemented checkout calculations, cart editing, receipt generation, and role-based authentication. The POS workflow is now significantly more functional and secure. Everything was tested to make sure the total calculations and the permissions for employees/managers were correct.
- Focus for the Next Sprint:
 - Add input validation and quantity safeguards.
 - Begin inventory reporting features.
 - Improve receipt formatting.
 - Add unit tests for checkout logic.
- PO/Stakeholder Review:
 - The Product Owner reviewed all completed tasks/backlog items:
 - Checkout calculations are accurate and update correctly.
 - Cart modification works without breaking totals.
 - Receipt generation reflects correct transaction data.
 - Role-based authentication properly restricts access.
 - Feedback Provided:
 - Add validation to prevent negative cart quantities.
 - Consider adding discount functionality in a future sprint.
 - Improve receipt formatting.
 - Priority Revisions:
 1. Validation improvements moved to the Sprint #3 backlog.
 2. Reporting features moved slightly lower in priority until the POS workflow is fully stabilized.

Sprint Retrospective:

- Changes in the Scrum Process:
 - Our team does not believe we need to make any changes to the Scrum Process yet, in the context of this Sprint.
- Start: Writing acceptance criteria in more detail before sprint planning. | Adding small unit tests during development.
- Stop: Nothing.

- Continue: Clear communication, frequent commits, and keeping standups short and focused.
- Other Planned Adjustments/Concerns:
 - No major concerns at this time.

Daily Standup #1:

- Duration: 5 Minutes
- Facilitator: Timyathus Spikes

=====

Tyrese Dickson

1. **What did I do yesterday?**
I wrapped up working on creating/finishing the database schema.
2. **What do I plan to do today?**
Today, I planned out how I was going to calculate the tax and totals upon checkout.
3. **What are any challenges or impediments that I have experienced?**
None

Timyathus Spikes

1. **What did I do yesterday?**
I wrapped up working on completing the basic UI framework.
2. **What do I plan to do today?**
Today, I planned out how I was going to add the ability to edit the cart by removing items for correction purposes.
3. **What are any challenges or impediments that I have experienced?**
None

Jason Gun

1. **What did I do yesterday?**
I wrapped up working on customizing/configuring the GitHub repository.
2. **What do I plan to do today?**
Today, I planned out how I was going to send the customer a receipt upon checkout.
3. **What are any challenges or impediments that I have experienced?**
None

Daniel Foister

1. **What did I do yesterday?**
I wrapped up working on fully setting up the Jira SCRUM board.
2. **What do I plan to do today?**
Today, I planned out how I was going to incorporate role-based authentication for inventory management and checkout.
3. **What are any challenges or impediments that I have experienced?**
None

Daily Standup #2:

- Duration: 5 Minutes
- Facilitator: Timyathus Spikes

=====

Tyrese Dickson

4. **What did I do yesterday?**

Yesterday, I planned out how I was going to calculate the tax and totals upon checkout.

5. **What do I plan to do today?**

Today, I am going to add the functionality where the product will calculate the tax and totals upon checkout, which I planned out during the last session.

6. **What are any challenges or impediments that I have experienced?**

Ran into some problems with calculating the tax, which caused this task to take longer than I would have liked.

Timyathus Spikes

4. **What did I do yesterday?**

Yesterday, I planned out how I was going to add the ability to edit the cart by removing items for correction purposes.

5. **What do I plan to do today?**

Today, I am going to insert the ability to edit the cart by removing items for correction purposes to the product, which I planned out during the last session.

6. **What are any challenges or impediments that I have experienced?**

None

Jason Gun

4. **What did I do yesterday?**

Yesterday, I planned out how I was going to send the customer a receipt upon checkout.

5. **What do I plan to do today?**

Today, I am going to add the ability to send the customer a receipt upon checkout, which I planned out during the last session.

6. **What are any challenges or impediments that I have experienced?**

None

Daniel Foister

4. **What did I do yesterday?**

Yesterday, I planned out how I was going to incorporate role-based authentication for inventory management and checkout.

5. **What do I plan to do today?**

Today, I am going to create/add the role-based authentication for inventory management and checkout, which I planned out during the last session.

6. **What are any challenges or impediments that I have experienced?**

I struggled to verify whether or not certain roles were actually restricted from performing admin/manager functions.

Daily Standup #3:

- Duration: 5 Minutes
- Facilitator: Timyathus Spikes

=====

Tyrese Dickson

7. **What did I do yesterday?**

I continued working on calculating the tax and totals upon checkout.

8. **What do I plan to do today?**

Complete my assigned task and plan for Sprint #3.

9. **What are any challenges or impediments that I have experienced?**

None

Timyathus Spikes

7. **What did I do yesterday?**

I continued working on the ability to edit the cart by removing items for correction purposes.

8. **What do I plan to do today?**

Complete my assigned task and plan for Sprint #3.

9. **What are any challenges or impediments that I have experienced?**

None

Jason Gun

7. **What did I do yesterday?**

I continued working on sending the customer a receipt upon checkout.

8. **What do I plan to do today?**

Complete my assigned task and plan for Sprint #3.

9. **What are any challenges or impediments that I have experienced?**

None

Daniel Foister

7. **What did I do yesterday?**

I continued working on incorporating role-based authentication for inventory management and checkout.


8. **What do I plan to do today?**

Complete my assigned task and plan for Sprint #3.

9. **What are any challenges or impediments that I have experienced?**

None

Exported Copy of Scrum Board:

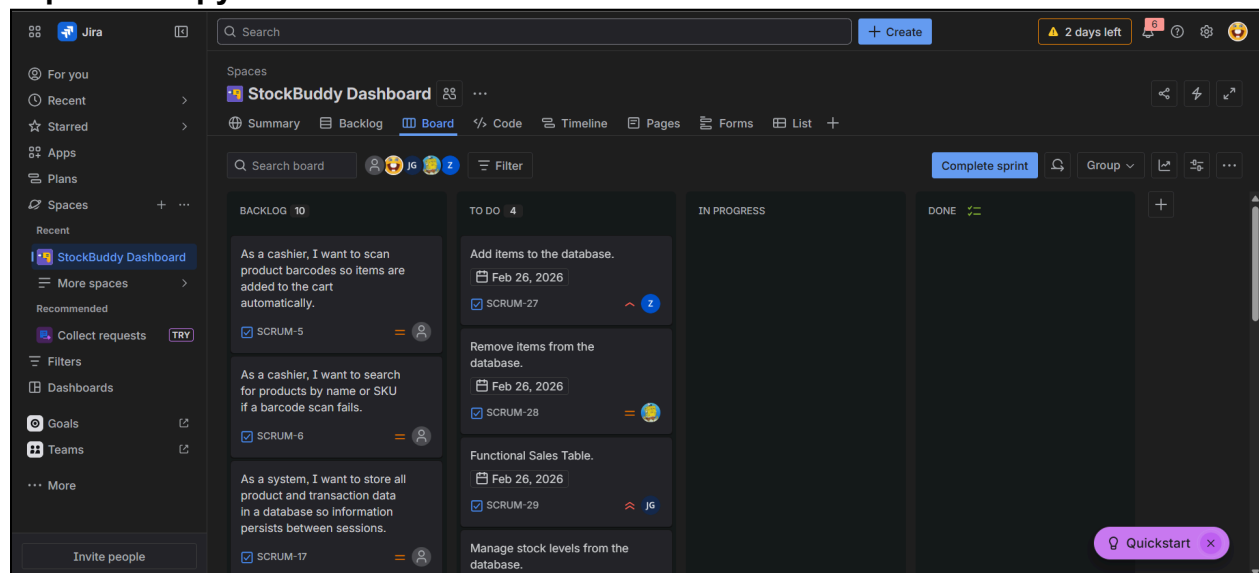

END.
