

Daniel Foister, Jason Gun, Timyathus Spikes, Tyrese Dickson - DTJT Group
Shehenaz Shaik
CSCI 4350
Sprint #1 - 2/5-2/12

Roles:

- Product Owner: Timyathus Spikes
- Scrum Master: Daniel Foister
- Development Team: Jason Gun, Tyrese Dickson

Time Limit: Two Days (2/5, 2/10, 2/12)

Sprint Goal:

- To establish a foundation for 'StockBuddy' by setting up the project repository, configuring the Jira board, creating the initial database schema, and implementing a basic UI framework. This sprint focused on ensuring the team has a stable/organized foundation to support feature development in future sprints.

User Stories/To-Do Chosen for Sprint:

- **SCRUM-19:** Database Schema Creation
- **SCRUM-20:** Basic UI Framework
- **SCRUM-21:** Project Repository Setup
- **SCRUM-22:** Jira Board Creation/Configuration

Total Sprint Duration:

- 4 members x 4 hours/week x 1 Week/Sprint = **16 man-hours available**

Tasks Performed:

- Task Name: Database Schema Creation
- Task Owner: Tyrese Dickson
- Planned Duration: 4 hours
- Actual Duration: 6 hours
- Status: Completed
- Challenges: Designing the relationships between products, users, and transactions to make sure they would support the future POS and reporting features.

- =====
- Task Name: Basic UI Framework
 - Task Owner: Timyathus Spikes
 - Planned Duration: 3 hours
 - Actual Duration: 7 hours
 - Status: Completed
 - Challenges: The initial layout took longer than I expected as our team made expanding decisions about how the UI needed to scale for our future sprints.
- =====

- Task Name: Project Repository Setup
- Task Owner: Jason Gun
- Planned Duration: 1 hour
- Actual Duration: 2 hours
- Status: Completed

- Challenges: None

=====

- Task Name: Jira Board Creation/Configuration
- Task Owner: Daniel Foister
- Planned Duration: 1 hour
- Actual Duration: 1 hour
- Status: Completed
- Challenges: None

=====

Sprint Review:

- Was the Sprint Goal Achieved?:
 - The Sprint Goal was Achieved.
 - Our DoD: Our work/code maps to all requirements specified in the Jira Board (backlog).
 - We successfully established the foundational components for our project. The repository and Jira board were fully configured, the initial database schema was created, and a basic UI framework was implemented. This sprint provides a stable base for our future development of 'StockBuddy.'
- Focus for the Next Sprint:
 - Begin implementing user authentication (login/logout features).
 - Start core inventory management features.
 - Add UI components for product handling.
- PO/Stakeholder Review:
 - The Product Owner reviewed all completed tasks/backlog items:
 - The database schema supports core entities (Users, Products, Transactions).
 - The UI framework is sufficient to begin implementing features.
 - The Jira board is properly structured and organized.
 - Feedback Provided:
 - The Product Owner requested that authentication be prioritized in Sprint #2.
 - Inventory management features should follow immediately after authentication.
 - Additional detail should be added to acceptance criteria in future backlog items to reduce ambiguity.
 - Priority Revisions:
 1. Authentication moved to the highest priority for Sprint #2.
 2. Inventory management stories moved ahead of reporting stories.

Sprint Retrospective:

- Changes in the Scrum Process:
 - Our team agreed that the Scrum process is working well so far, given how we functioned last semester. However, we identified some opportunities to improve task estimation and coordinate our version control.
- Start: Committing code more frequently to reduce merge conflicts, and add clearer task descriptions in Jira.
- Stop: Underestimating task complexity during planning.

- Continue: Strong communication during sessions, clear role responsibilities, and good collaboration.
- Other Planned Adjustments/Concerns:
 - We do not have any other planned adjustments or concerns right now.

Daily Standup #1:

- Duration: 5 Minutes
- Facilitator: Daniel Foister

=====

Tyrese Dickson

1. **What did I do yesterday?**
I did nothing because of the class cancellation.
2. **What do I plan to do today?**
Today, I am planning the structure of the database schema, outlining the necessary tables and relationships before implementation begins.
3. **What are any challenges or impediments that I have experienced?**
None

Timyathus Spikes

1. **What did I do yesterday?**
I did nothing because of the class cancellation.
2. **What do I plan to do today?**
Today, I am planning the basic UI framework by organizing the layout and navigation flow that will support the core functionality of the application.
3. **What are any challenges or impediments that I have experienced?**
None

Jason Gun

1. **What did I do yesterday?**
I did nothing because of the class cancellation.
2. **What do I plan to do today?**
Today, I am planning the project repository setup, including the structure for version control, branching strategy, and collaboration workflow for the team.
3. **What are any challenges or impediments that I have experienced?**
None

Daniel Foister

1. **What did I do yesterday?**
I did nothing because of the class cancellation.
2. **What do I plan to do today?**
Today, I am planning the creation and configuration of the Jira board to properly organize sprint tasks and workflow tracking for the team.
3. **What are any challenges or impediments that I have experienced?**
None

Daily Standup #2:

- Duration: 5 Minutes
- Facilitator: Daniel Foister

=====

Tyrese Dickson

4. **What did I do yesterday?**

I continued working on creating/finishing the database schema.

5. **What do I plan to do today?**

Complete my assigned task and plan for Sprint #2.

6. **What are any challenges or impediments that I have experienced?**

None

Timyathus Spikes

4. **What did I do yesterday?**

I continued working on completing the basic UI framework.

5. **What do I plan to do today?**

Complete my assigned task and plan for Sprint #2.

6. **What are any challenges or impediments that I have experienced?**

None

Jason Gun

4. **What did I do yesterday?**

I continued working on customizing/configuring the GitHub repository.

5. **What do I plan to do today?**

Complete my assigned task and plan for Sprint #2.

6. **What are any challenges or impediments that I have experienced?**

None

Daniel Foister

4. **What did I do yesterday?**

I continued working on fully setting up/refamiliarizing myself with the Jira SCRUM board.


5. **What do I plan to do today?**

Complete my assigned task and plan for Sprint #2.

6. **What are any challenges or impediments that I have experienced?**

None

Exported Copy of Scrum Board:

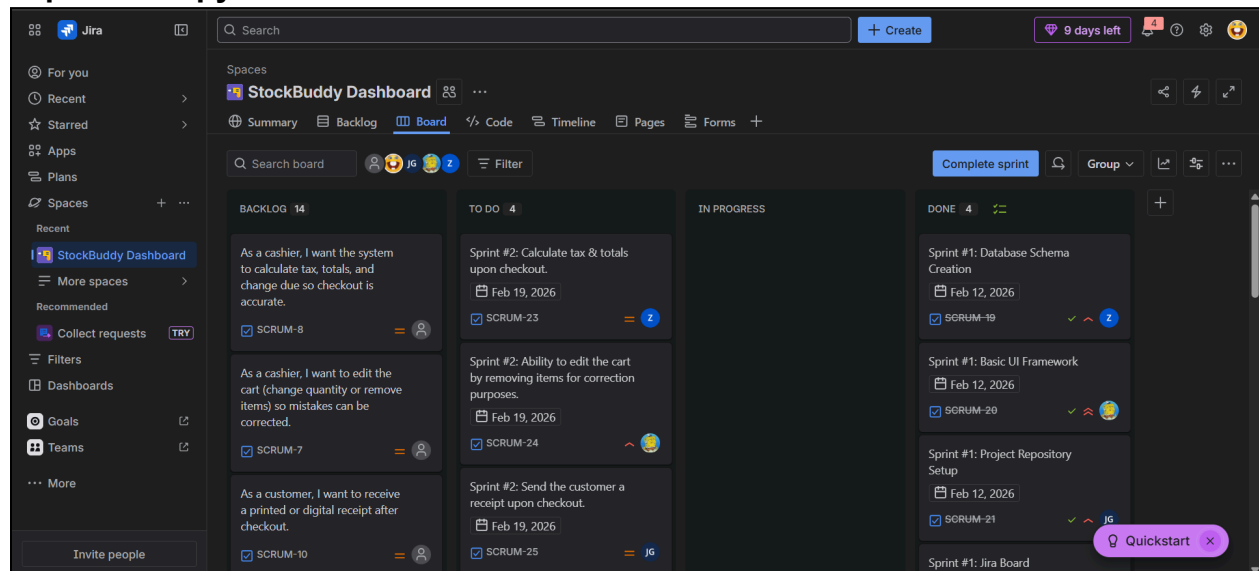

END.
